

Springfield Union Station

Project Update - July 2016

Work Completed and Underway


- All canopy work is complete
- Granite curbing 70% complete
- Tunnel waterproofing Phases 2 and 3 are complete
- Ceramic tile work of restrooms on the 2nd floor is complete
- Ceramic tile work of restrooms on the 3rd floor is in progress
- Framing of concourse ceilings complete
- Concourse wall and ceiling wood blocking is complete
- Concourse column cement board at base for marble is in progress
- Electrical conduit and CCTV conduit in progress
- Elevator installation work has started
- Rail painting is underway



07/16 - Workers install concrete for the busway



07/16 - A new sidewalk is installed under the island canopy

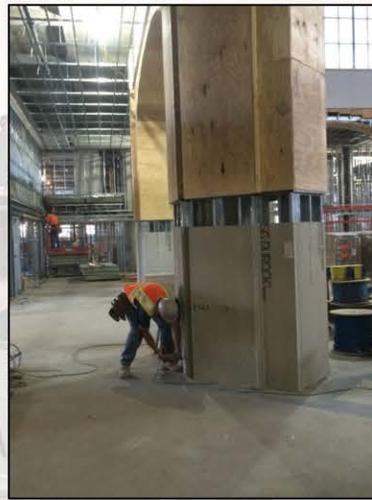

07/16 - Workers install cement board to the Terminal columns to hold the new marble



07/16 - Wood blocking is applied to the ceiling and walls to accommodate future plaster moldings.

Upcoming Work

- Installation of plumbing fixtures inside Terminal Building
- Drywall Installation for Stairway 2
- Terminal arches to be sheetrocked and taped
- Curtain wall glazing to be installed in Parking Garage
- Parking Garage railing to be painted
- Light fixtures installed in Parking Garage
