

Springfield Union Station

Project Update - June 2016

Work Completed and Underway


- Rough-in of mechanical, plumbing, fire protection and electrical piping in progress
- 1st floor and Mezzanine wall framing and drywall in progress
- Tunnel waterproofing Phase 2 is 95% complete
- Ductwork connections for HVAC roof top units is on going
- Ceramic tile work of restrooms on the 2nd floor is in progress
- Framing and drywall of stairway 2 in progress
- Framing of concourse ceilings complete
- Framing of concourse walls and arches is complete
- West elevation brick work complete and staging has been removed
- Electrical conduit near completion, CCTV conduit in progress



06/16 - Wood blocking added to ceiling and walls for future plaster moldings



06/16 - A new sidewalk is installed under the walkway canopy

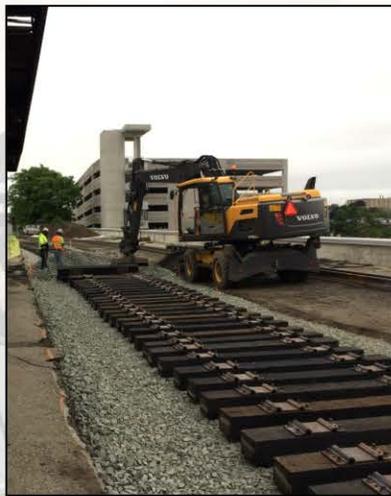

06/16 - The Shoo-fly track installation is almost complete



06/16 - View of the site including west wall of the Terminal Building now that the scaffolding has been removed.

Upcoming Work

- Installation of plumbing fixtures inside Terminal
- Drywall Installation for Stairway 2 in Terminal Building
- Concourse arches will be sheetrocked and taped
- 2nd and 3rd floor Restrooms will be tiled
- Completion of 1st floor framing
- 1st floor Electrical work inspected and approved
- Curtain wall glazed, light fixtures installed, rough-in of electrical, railings painted in Parking Garage
