


Springfield Union Station

Project Update - August 2016

Work Completed and Underway

- Rough-in of mechanical, plumbing, fire protection near completion
- 1st floor and Mezzanine wall framing complete, drywall in progress
- Granite curbing 80% complete
- Terrazzo restoration has begun
- Ceramic tile work of restrooms on the 2nd and 3rd floor is complete
- Concourse wood blocking complete, drywall in progress
- Elevators 1 and 2 installation in progress
- Painting of offices is in progress
- Bus shelter installation in progress
- Bus way concrete complete
- Electrical and CCTV conduit near completion in Parking Garage

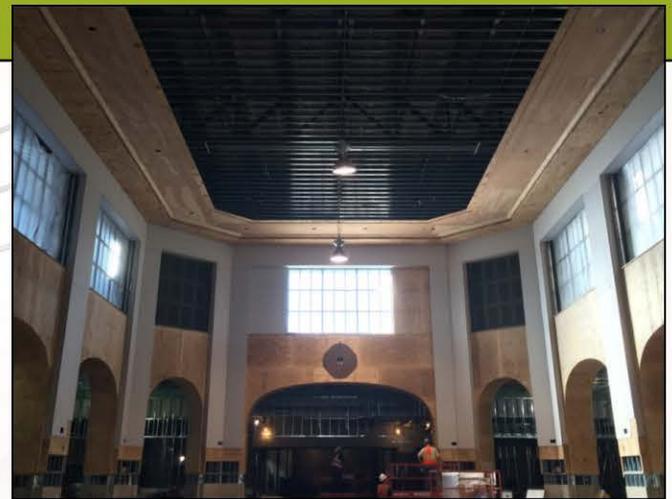

08/16 - Workers complete the wood blocking to the walls and drywall phase has begun



08/16 - Electricians begin to install the new light poles



08/16 - Workers install the first section of Glass Fiber Reinforced Concrete (GFRC) to the side of the Terminal Building



08/16 - The new bike rack is installed

Upcoming Work

- Drywall installation for Stairway 2 in Terminal Building
- Concourse arches will be sheet-rocked and taped
- Plastering of Main Concourse ceiling to commence
- Terminal Building doorframes to be installed
- Termination of mechanical, electrical, fire protection, and plumbing equipment and devices in Parking Garage
- Installation of architectural metal panels in Garage
