


EXHIBIT 1h: PROPOSED SCHEDULE

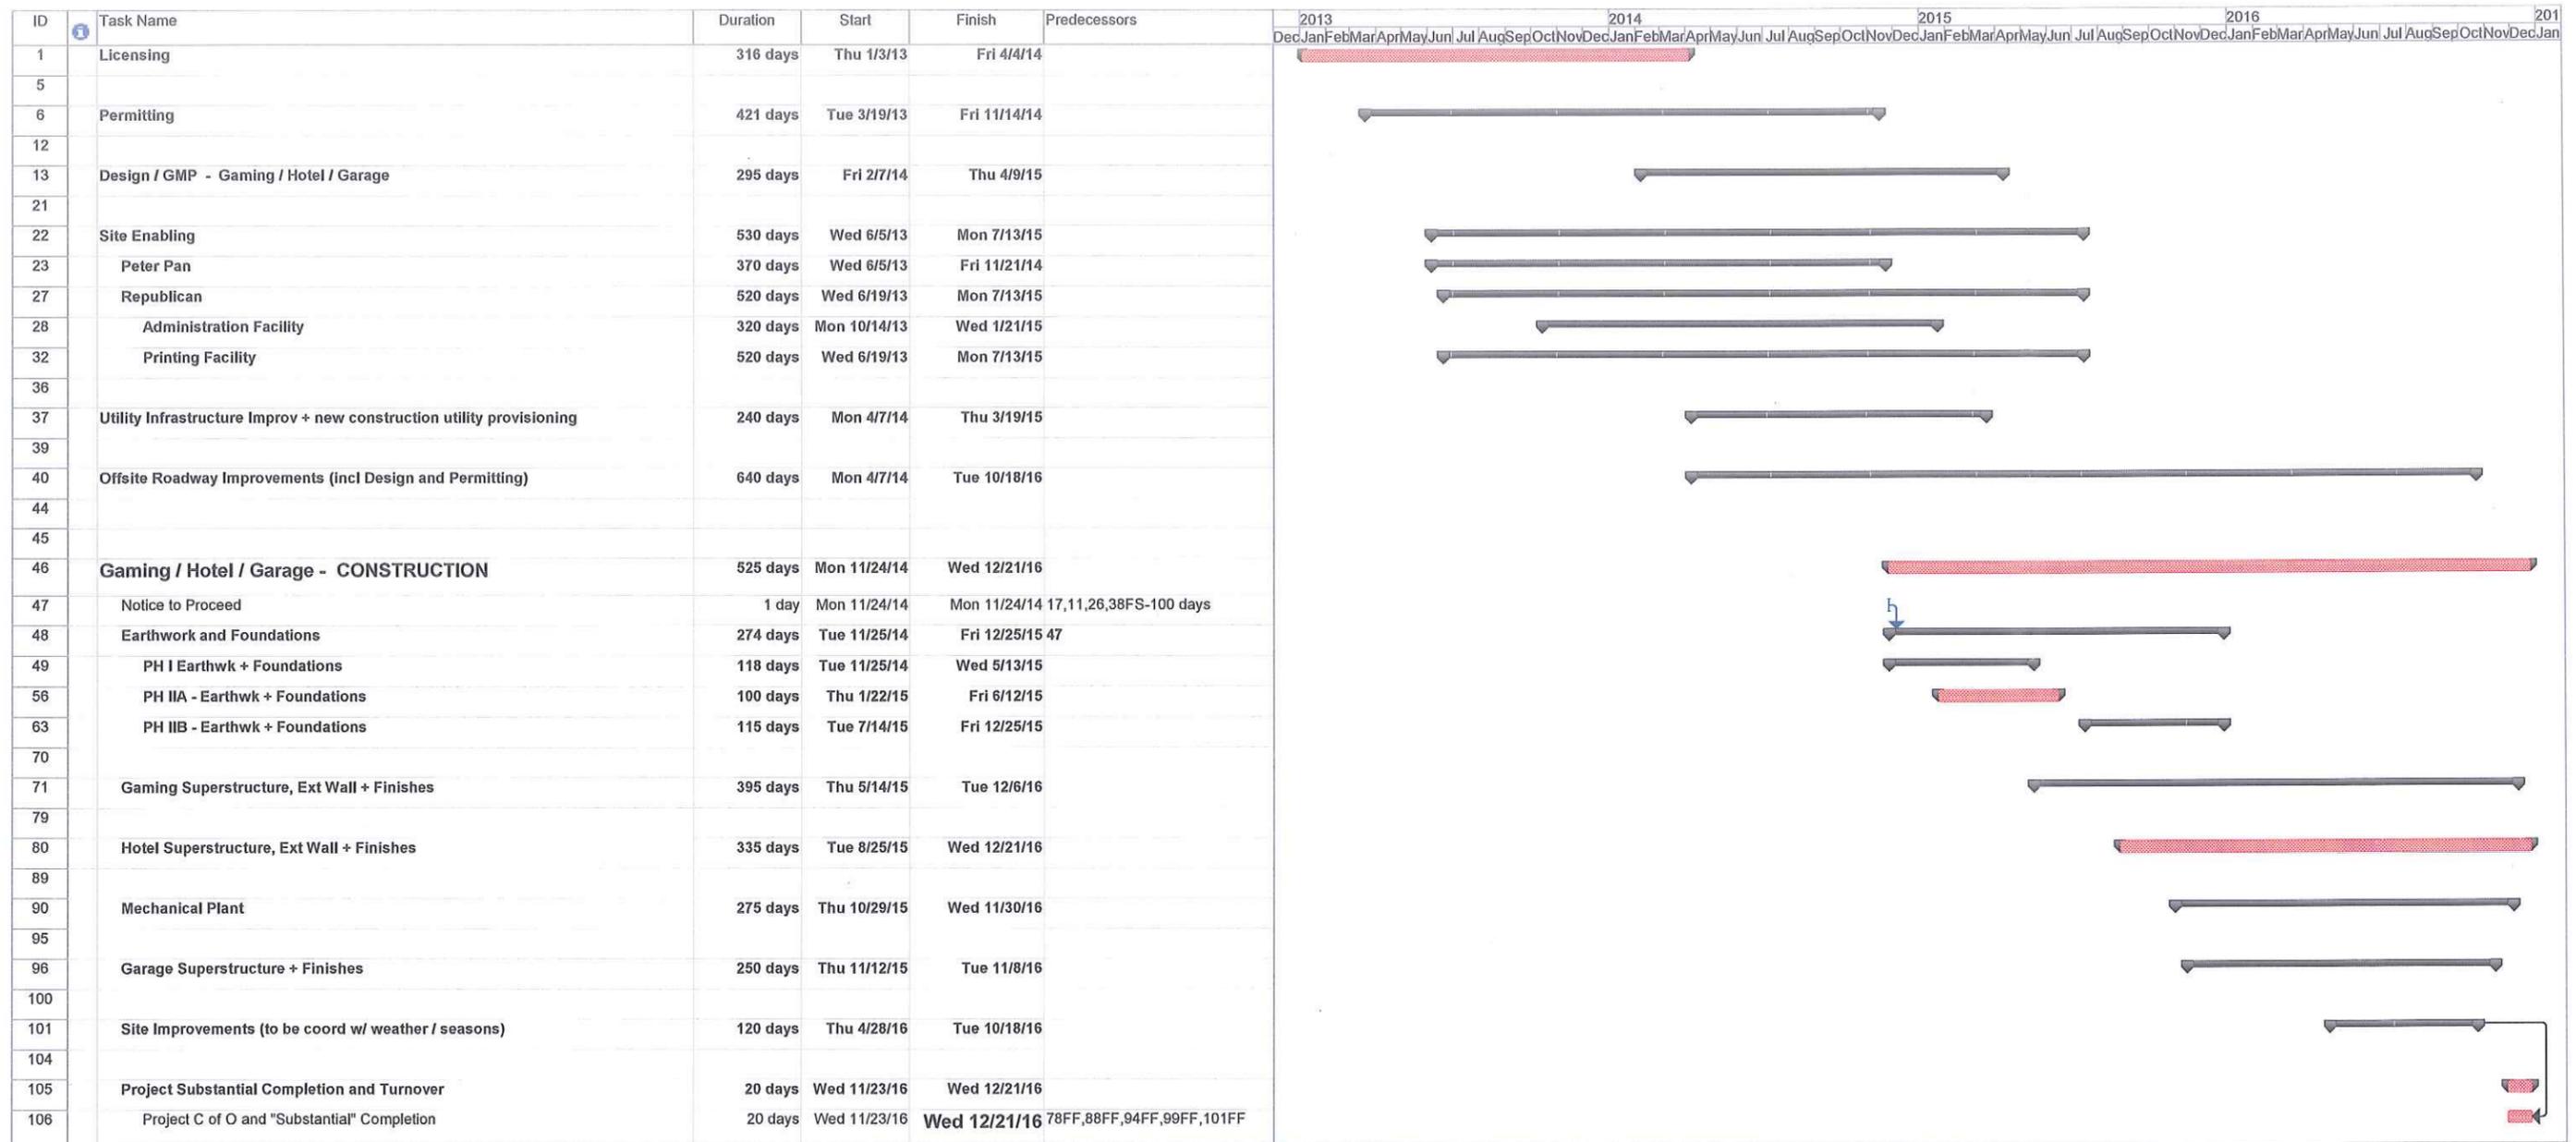

Project: PennRFQ12-8-12
Date: Fri 12/28/12



EXHIBIT 1h: PROPOSED CONSTRUCTION PHASING PLAN

We propose the following construction phasing plan for this Project:

PHASE 1

Phase 1 mobilization includes the relocation, demolition and abatement of of the current onsite bus facility.

Start of construction of the Gaming

PHASE 2A

Phase 2a mobilization includes the relocation, abatement, utility separataion, and temporary facade/ demolition of the south "administration" part of the Republican.

Temporary space and fitout of the space for the "administration" of the Republican is required prior to this phase.

Start of construction of the Hotel

PHASE 2B

Phase 2b mobilization includes the relocation and demolition of the north "printing" part of the Republican.



Construction of a new printing facility for the Republican is required prior to this phase.

Start of construction of the Garage



EXHIBIT 1h: WE WILL BE A GOOD NEIGHBOR TO THE SURROUNDING BUSINESSES & COMMUNITY

Our mission is to responsibly plan construction project operations, means, and methods which create a positive impact on the surrounding community and environment. We have identified local businesses surrounding the proposed site to highlight our understanding of the area and to ensure that our top priority is to mitigate the impact the construction of the casino will have on the businesses, neighbors and the community.

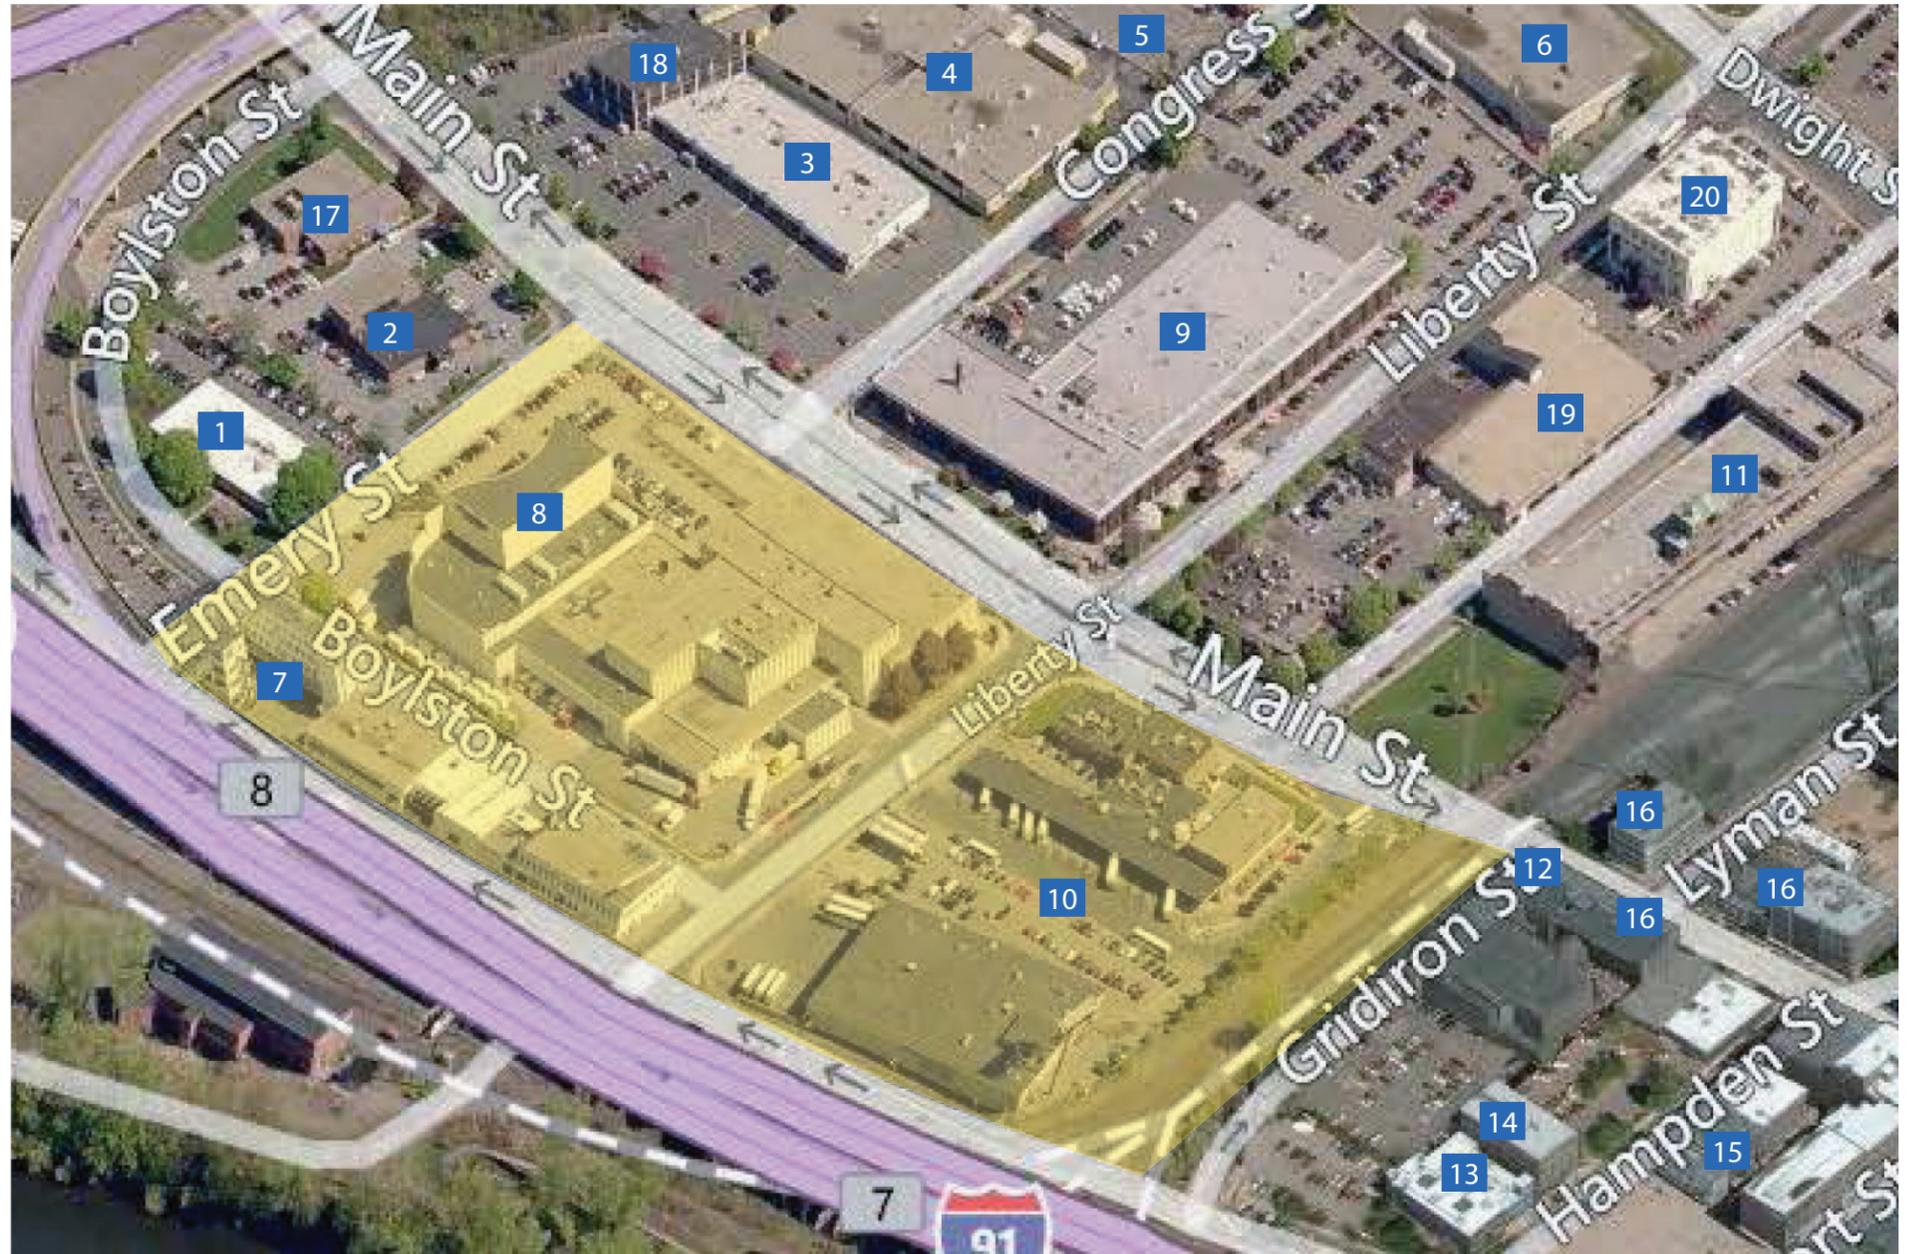

- | | | |
|--|------------------------------|---|
| 1. Hampden County Physicians Association | 8. <i>The Republican</i> | 18. The Vet Center |
| 2. Freedom Credit Union | 9. US Post Office | 19. Liberty Street Shops |
| 3. Northgate Plaza: H&R Block, WIC, Northgate Medical, Hanger Prosthetics | 10. Peter Pan Bus lines | 20. Diagnostic Imaging and Mecal Center |
| 4. Uncle Bob's Self Storage | 11. Amtrak, Union Station | |
| 5. Pioneer Valley Planning Commission | 12. The Paramount | |
| 6. Benchmark Carbide, a Division of Custom Carbide Corporation | 13. New England Public Radio | |
| 7. Mostly vacant, formerly Kittredge Foodservice Equipment & Supplies and WTGBY TV (PBS Station) | 14. The Whitcomb Building | |
| | 15. Patton Building | |
| | 16. Downtown Shops | |
| | 17. The Kidney Center | |

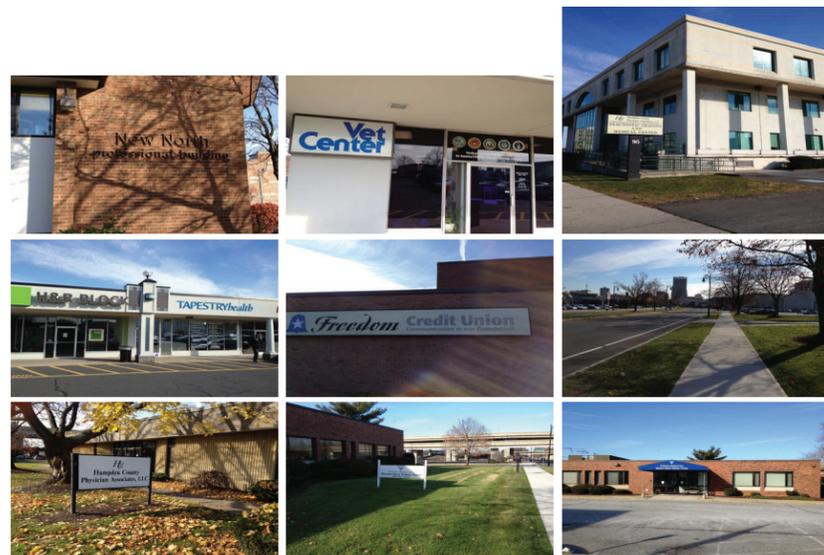


EXHIBIT 1h: ANTICIPATED POTENTIAL TRUCK ROUTING

Traffic plans will route trucks appropriately to minimize the congestion on local roads and to mitigate the impact on local businesses.

The close proximity to the proposed casino site is a benefit to these local businesses as they will generate more business from the increased activity in the surrounding area.

- **Route from the West:** Straight over Route 20 West Bridge Onto Main Street
- **Route from the South:** Exit 8 from 91 North to Dwight Street. Turn right onto Liberty Street
- **Route from the North:** Exit 9a from Route 91 South
- **Route from the East:** Exit 2B on 291 East to Dwight Street. Turn right onto Liberty Street. (Feeds from 90 Mass Pike)

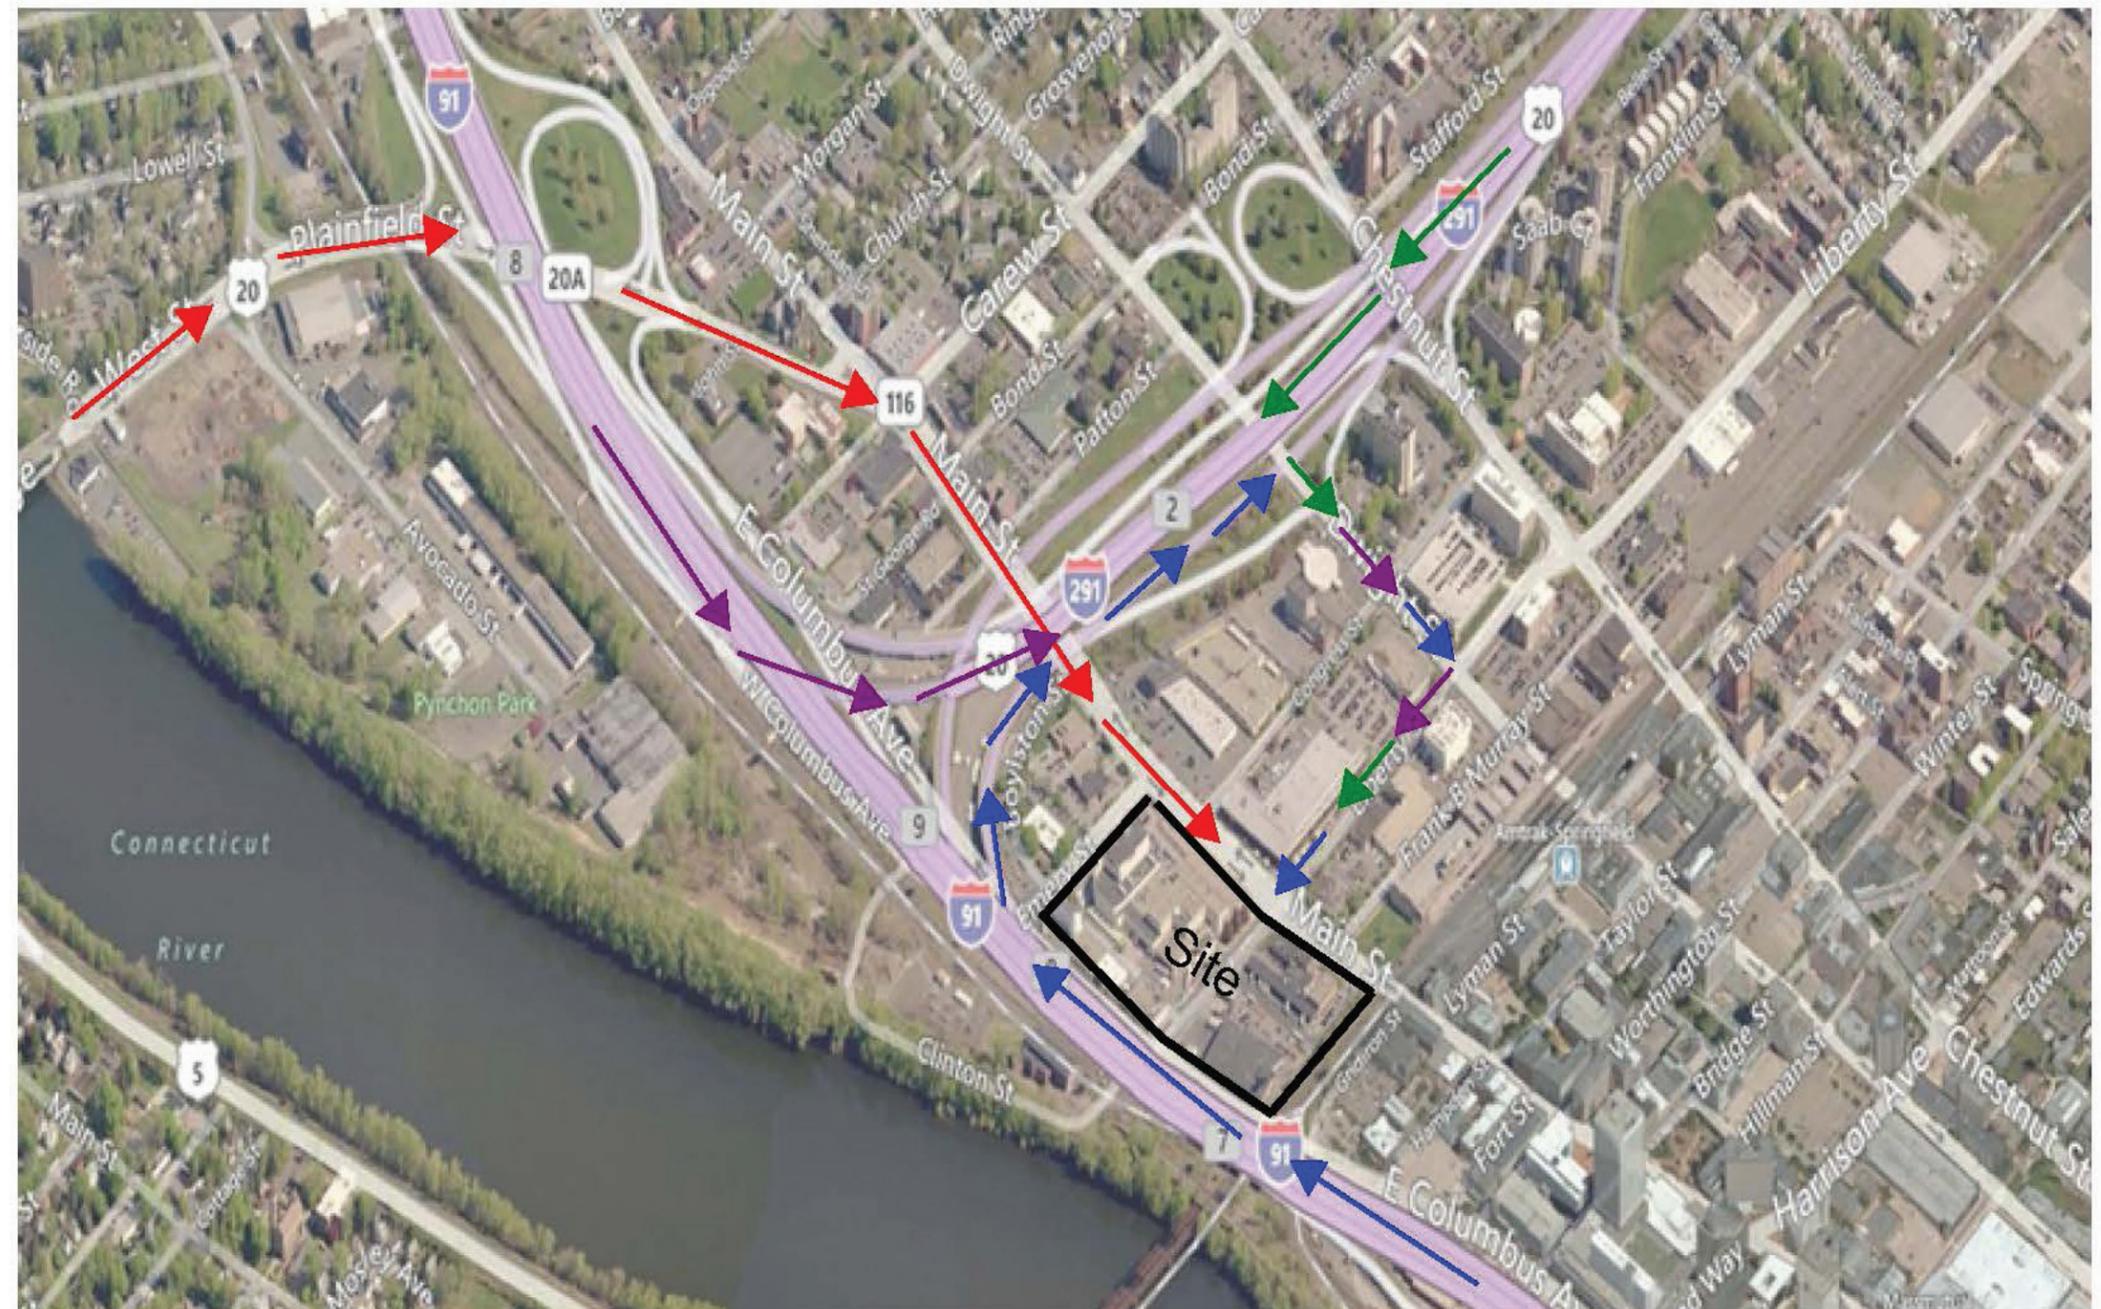


EXHIBIT 1h: MILESTONE LOGISTICS PLANS

PHASE 1 START

Site Fence Around Phase 1

Demo Begins on Peter Pan



ALL PHASES IN PROGRESS

Gaming: Superstructure Complete/Envelope Begins
 – Interior Fit out Underway

Hotel: Steel Superstructure Complete
 – Interior Fit out Underway

Garage: Piles/Foundation Complete
 – Precast Erection Begins




PHASE 2a START

Gaming Floor Excavation Begins

Demo on Admin Portion of Republican Begins

Gaming Floor Piles Begin

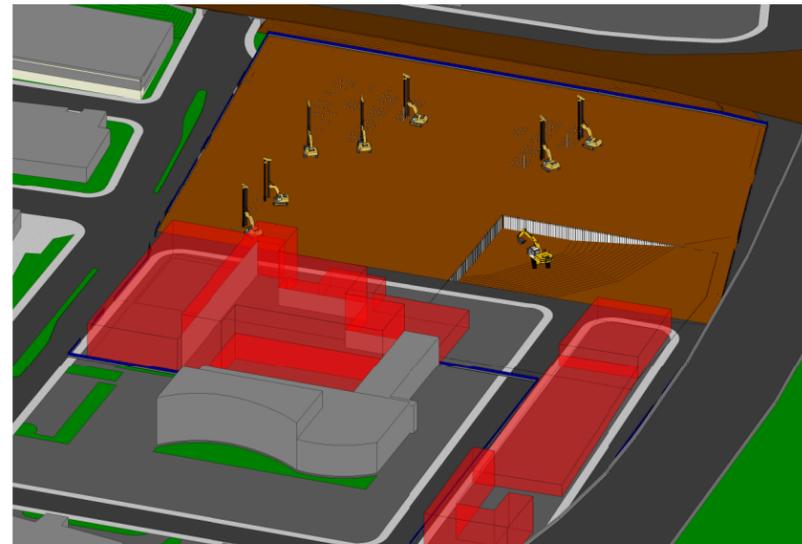

ALL PHASES IN PROGRESS

Hotel+Gaming: Envelope Complete
 – Interior Fit out Underway

Garage: Precast Underway
 MEP and Finsihes Underway




PHASE 1 AND 2a ONGOING

Excavation Complete on Gaming/Hotel

Gaming/Hotel Piles and Foundations Complete

Gaming Superstructure Underway

Printing Portion of Republican Demo

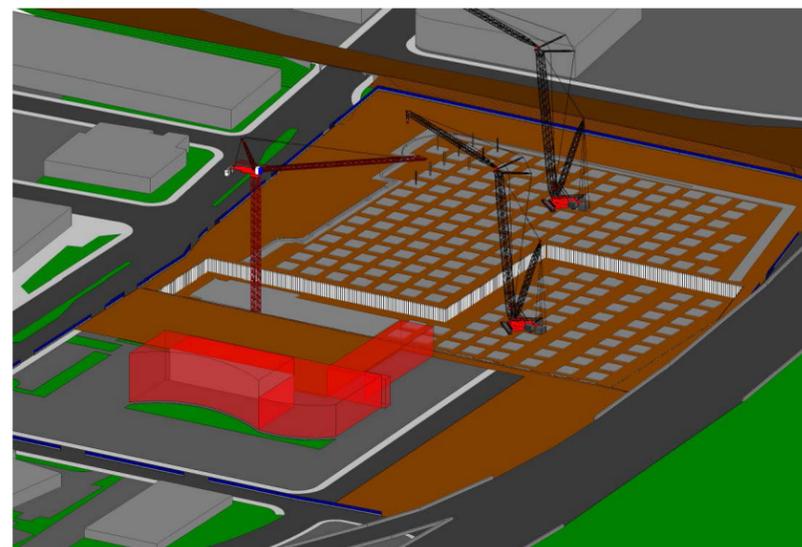

ALL PHASES COMPLETE

January 1, 2017

