


Springfield Union Station

Project Update - August 2015

Work Completed and Underway

- Completed installation of micro-piles in Terminal Building for elevator support
- Continued masonry work both inside and outside the Terminal Building, south, west and north elevations
- Completed installing the Aggregate Piers in the Busway
- Completed installation of new electric vault which replaces the existing substandard vault
- Vehicle barrier on top of retaining wall nearly complete

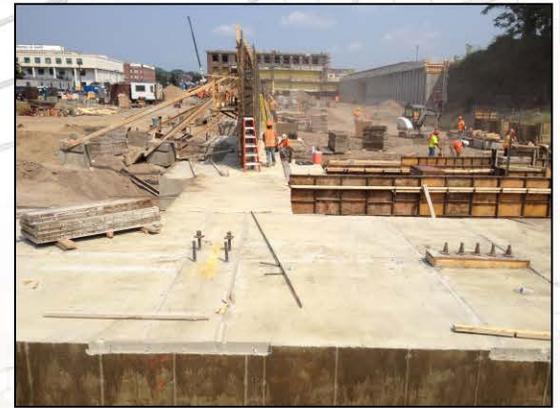

8/15 - The first concrete pile cap has been placed and the formwork is being installed for the next concrete placement.



8/15 - Sewer and water lines to the Terminal Building are being installed



8/15 - Canopy bases for the PVTA island can be seen here.

Upcoming Work

- Continuing to install forms and place concrete for cast in place (CIP) pile caps
- Installation of storm drainage in Liberty Street Connector, Frank B. Murray Street and Busway.
- Subgrade preparation and utility installation in Busway
- Sewer connection and water connections to Terminal Building
- Installing canopy bases and bus shelter bases
